


NORTH WESTERN RAILWAY

SYSTEM MAP AS ON 17.06.2017

SANCTIONED WORKS (IN PROGRESS NOT COMMISSIONED)

Sr. No.	NAME OF WORK	SALIENT FEATURES			PHYSICAL PROGRESS & TDC
		YEAR OF SANCTION	COST IN CR	LENGTH IN KMS	
1.0 NEW LINE (07)					
1.1	DAUSA(DO) -GANGAPUR CITY(GGC) (i)Revised Estimate of Rs780.98cr sanction by Rly Bd.on 07.03.17.	1996-97	780.98	92.67	53% 1.DO-Deedwana, June 17 2.GGC-Khuntha, Feb 18
1.2	RATLAM(RTM)-DUNGARPUR(DNRP)-Via-BANSWARA(BNSW) (i)Rly. Bd. vide letter dt. 30.03.17 directed to freeze all works.	2011-12	2417.24	188.85	6.25% Not fixed
1.3	THIAYAT HAMIRA(THM)-SANU (i)Land aquisition for forest & private land is still in progress. (ii)NOC for construction of ROB is still awaited from State Govt	2013-14	262.46	58.00	25% Jan 18
1.4	AJMER(AII)-KOTA(KTT)(NASEERABAD(NSD)-JALINDRI) (i)CCEA sanction is yet to be obtained by Rly Bd.	2013-14	822.00	145.00	Not fixed
1.5	PUSHKAR(POHT)-MERTA(MTD) (i)CCEA sanction is yet to be obtained by Rly Bd.	2013-14	323.00	59.00	Not fixed
1.6	AJMER(NASIRABAD)-SAWAI MADHOPUR(SWM) (CHAUTH KA BARWARA) (CKB)VIA TONK (i)Chief Secy./Govt. of Raj. vide D.O.letter no.F-26(7)-para/RC/2013/25409 Dt.09.12.2016 requested railways to share full cost of sanctioned works in progress & others future projects. (ii)State Govt. has refused to share the cost of project.	2015-16	873.71	165.00	Not fixed
1.7	TARANGHILL(TRAH) - ABU ROAD (ABR)VIA AMBAJI (i)Sanctioned in PB 2017-18 (ii)Hilly terrain (iii)DPR under preparation.	2017-18	1695.72	89.38	Not fixed
2.0 GAUGE CONVERSION WORKS (04)					
2.1	MAVLI Jn(MVJ)-BARI SADR(BI) (i)Section closed on 01.11.2016 for GC works. (ii)Huge qty. of EW of 330000 CUM, 87 LHS, 127 Bridges, 30.00 Km Retaining wall & 100 FB welds.	2013-14	295.02	82.01	11% 1.MVJ-BNNR, Jan 18 2.BNNR-BI, May 18
2.2	JAIPUR(JP)-SIKAR(SIKR) & SIKAR(SIKR)-CHURU(CUR) (i)Sikar - Fatehpur Shekhawati section part of Sikar-Churu CRS inspection done in Mar 17.	2008-09	658.07	320.04	60% 1.FPS-CUR, July 2017. 2.SIKR-PLSN, Dec 17 3.PLSN-RGS, June 18 4.RGS-JP, Mar 19
2.3	HIMMATNAGAR(HMT)-UDAIPUR(UDZ) (i)Acquisition of 47.51 Hq is pending, out of which 43.44Hq is forest land. (ii)38 Major & 352 minor bridges to be constructed. (iii)25.36 cu of EW (iv)20 nos. Stn. Bldg and 3 nos. PFs (v)37800 F.B. welds	2008-09	829.74	208.08	65% 1.UDZ-KRCD Feb 18 2.RGQ-HMT, Feb 18
2.4	MARWAR(MJ) - MAVLI(MVJ)(NATHDWARA) (i).Sanctioned in PB 2017-18 (ii).Hilly Terrian. (iii)DPR under preparation.	2017-18	1597.12	152.00	Not fixed
3.0 DOUBLING (06)					
3.1	AJMER(AII) - BANGURGRAM(BNGM) (i)Composite Cotract awarded on 24.06.2016, costing:113.38cr	2011-12	218.39	48.43	20% 1.BNGM-MLI, Jan 18. 2. AII-MLI, Feb 19
3.2	GURIYA(GRI)-MARWAR Jn(MJ) (i)MJ-SOD commissioned in Feb 2017. (ii)SOD-GRI CRS conducted on Mar 17. (iii)SOD-CNL Commissioned on April 17	2011-12	206.22	43.50	97% 1. CNL-GRI, June 17
3.3	BANGURGRAM(BNGM) - GURIYA(GRI) (i)Detailed Estimate sanctioned by C.A.(AGM/NWR) on 25.04.2016 (ii)Composite contract, costing 174.00cr, awarded on 11.11.2016.	2012-13	348.55	47.00	02% 1. HP-GRI, Dec 17 2. BNGM-HP Feb 19
3.4	RANI(RN)-MARWAR Jn(MJ). (i)RDSO cleared arrangement of BOX culvert, in 05 major Bridges. (ii)Commissioning of LHS requires completion of LHS work by DFCCIL in their part.	2012-13	335.53	51.82	18% 1. BWA-MJ, Jan 18 2. RN-BWA, Mar 19
3.5	ALWAR(AWR)- BANDIKUI(BKI) (i)Composite contract amounting Rs.118.24cr awarded on 18.05.2016	2013-14	281.03	60.37	24% 1. AWR-DGW, Feb 18 2. DGW-BKI, Mar 19
3.6	PHULERA(FL)-DEGANA(DNA) (i)Project is notified as Special Railway Project. (ii)EPC tender opened and RFQ finalized on 17.03.17.& RFP will be finalize by 2.8.17.	2015-16	611.53	108.00	0% 1. FL-DNA Feb 19
4.0 DOUBLING (RVNL) (06)					
4.1	ABU ROAD(ABR)- SAROTRA ROAD (SZA) (i)Maval(MAA)-Sri Amirgarh(SIM)-Sarotra Road(SZA) Mid Section work completed	2010-11	201.41	23.12	75% 1.ABR-MAA, March 18 2. MAA-SIM-SZA, Oct 17.
4.2	SWROOPGANJ(SRPJ)- ABU ROAD(ABR) (i) SRPJ-BMN commissioned on May 17.	2010-11	154.55	25.36	95% 1. SRPJ-BMNW April 17. 68% 2. BMN-ABR, March 18.
4.3	SAROTRA ROAD(SZA)-KARJODA(KRJD) (i)Mid Section work in Iqbalgarh(IQG)-Jethi(JTY)-Chitrasani(CTT)-Karjoda(KRJD)completed. Work is in progress in SZA-IQG sect (ii) There is a important bridge in JTY-CTT section	2010-11	194.13	23.59	69% 1. SZA-JETHI, Sept 17 2. JETHI-KRJD, Dec 18
4.4	RANI(RN)-KESHAVGANJ(KVJ) (i)MOI-KTR-NANA-KVJ commissioned on 15.03.2016. (ii)Mid Section work in RN-KZQ-FA-BRLY-JWB-MOI completed (iii)RN-KZQ will be commissioned alongwith RN-MJ NWR/Con work	2011-12	280.17	59.50	95% 1.KZQ-FA-BRLY-JWB-MOI June 17
4.5	REWARI(RE)-MANIHERU(MHU) (i)Rewari(RE)-Kosli(KSI) Commissioned on 05.03.17.. (ii)In Kosli(KSI)-Manheru(MHU) work is in progress.	2011-12	373.61	69.02	90% 1.KSI-JRL, June 17 2.JRL-MHU, Dec 17.
4.6	KARJODA(KRJD)-PALANPUR(PNU) (i)Work is in progress.	2011-12	26.00	5.40	98% 1. KRJD-PNU, Sept 17.

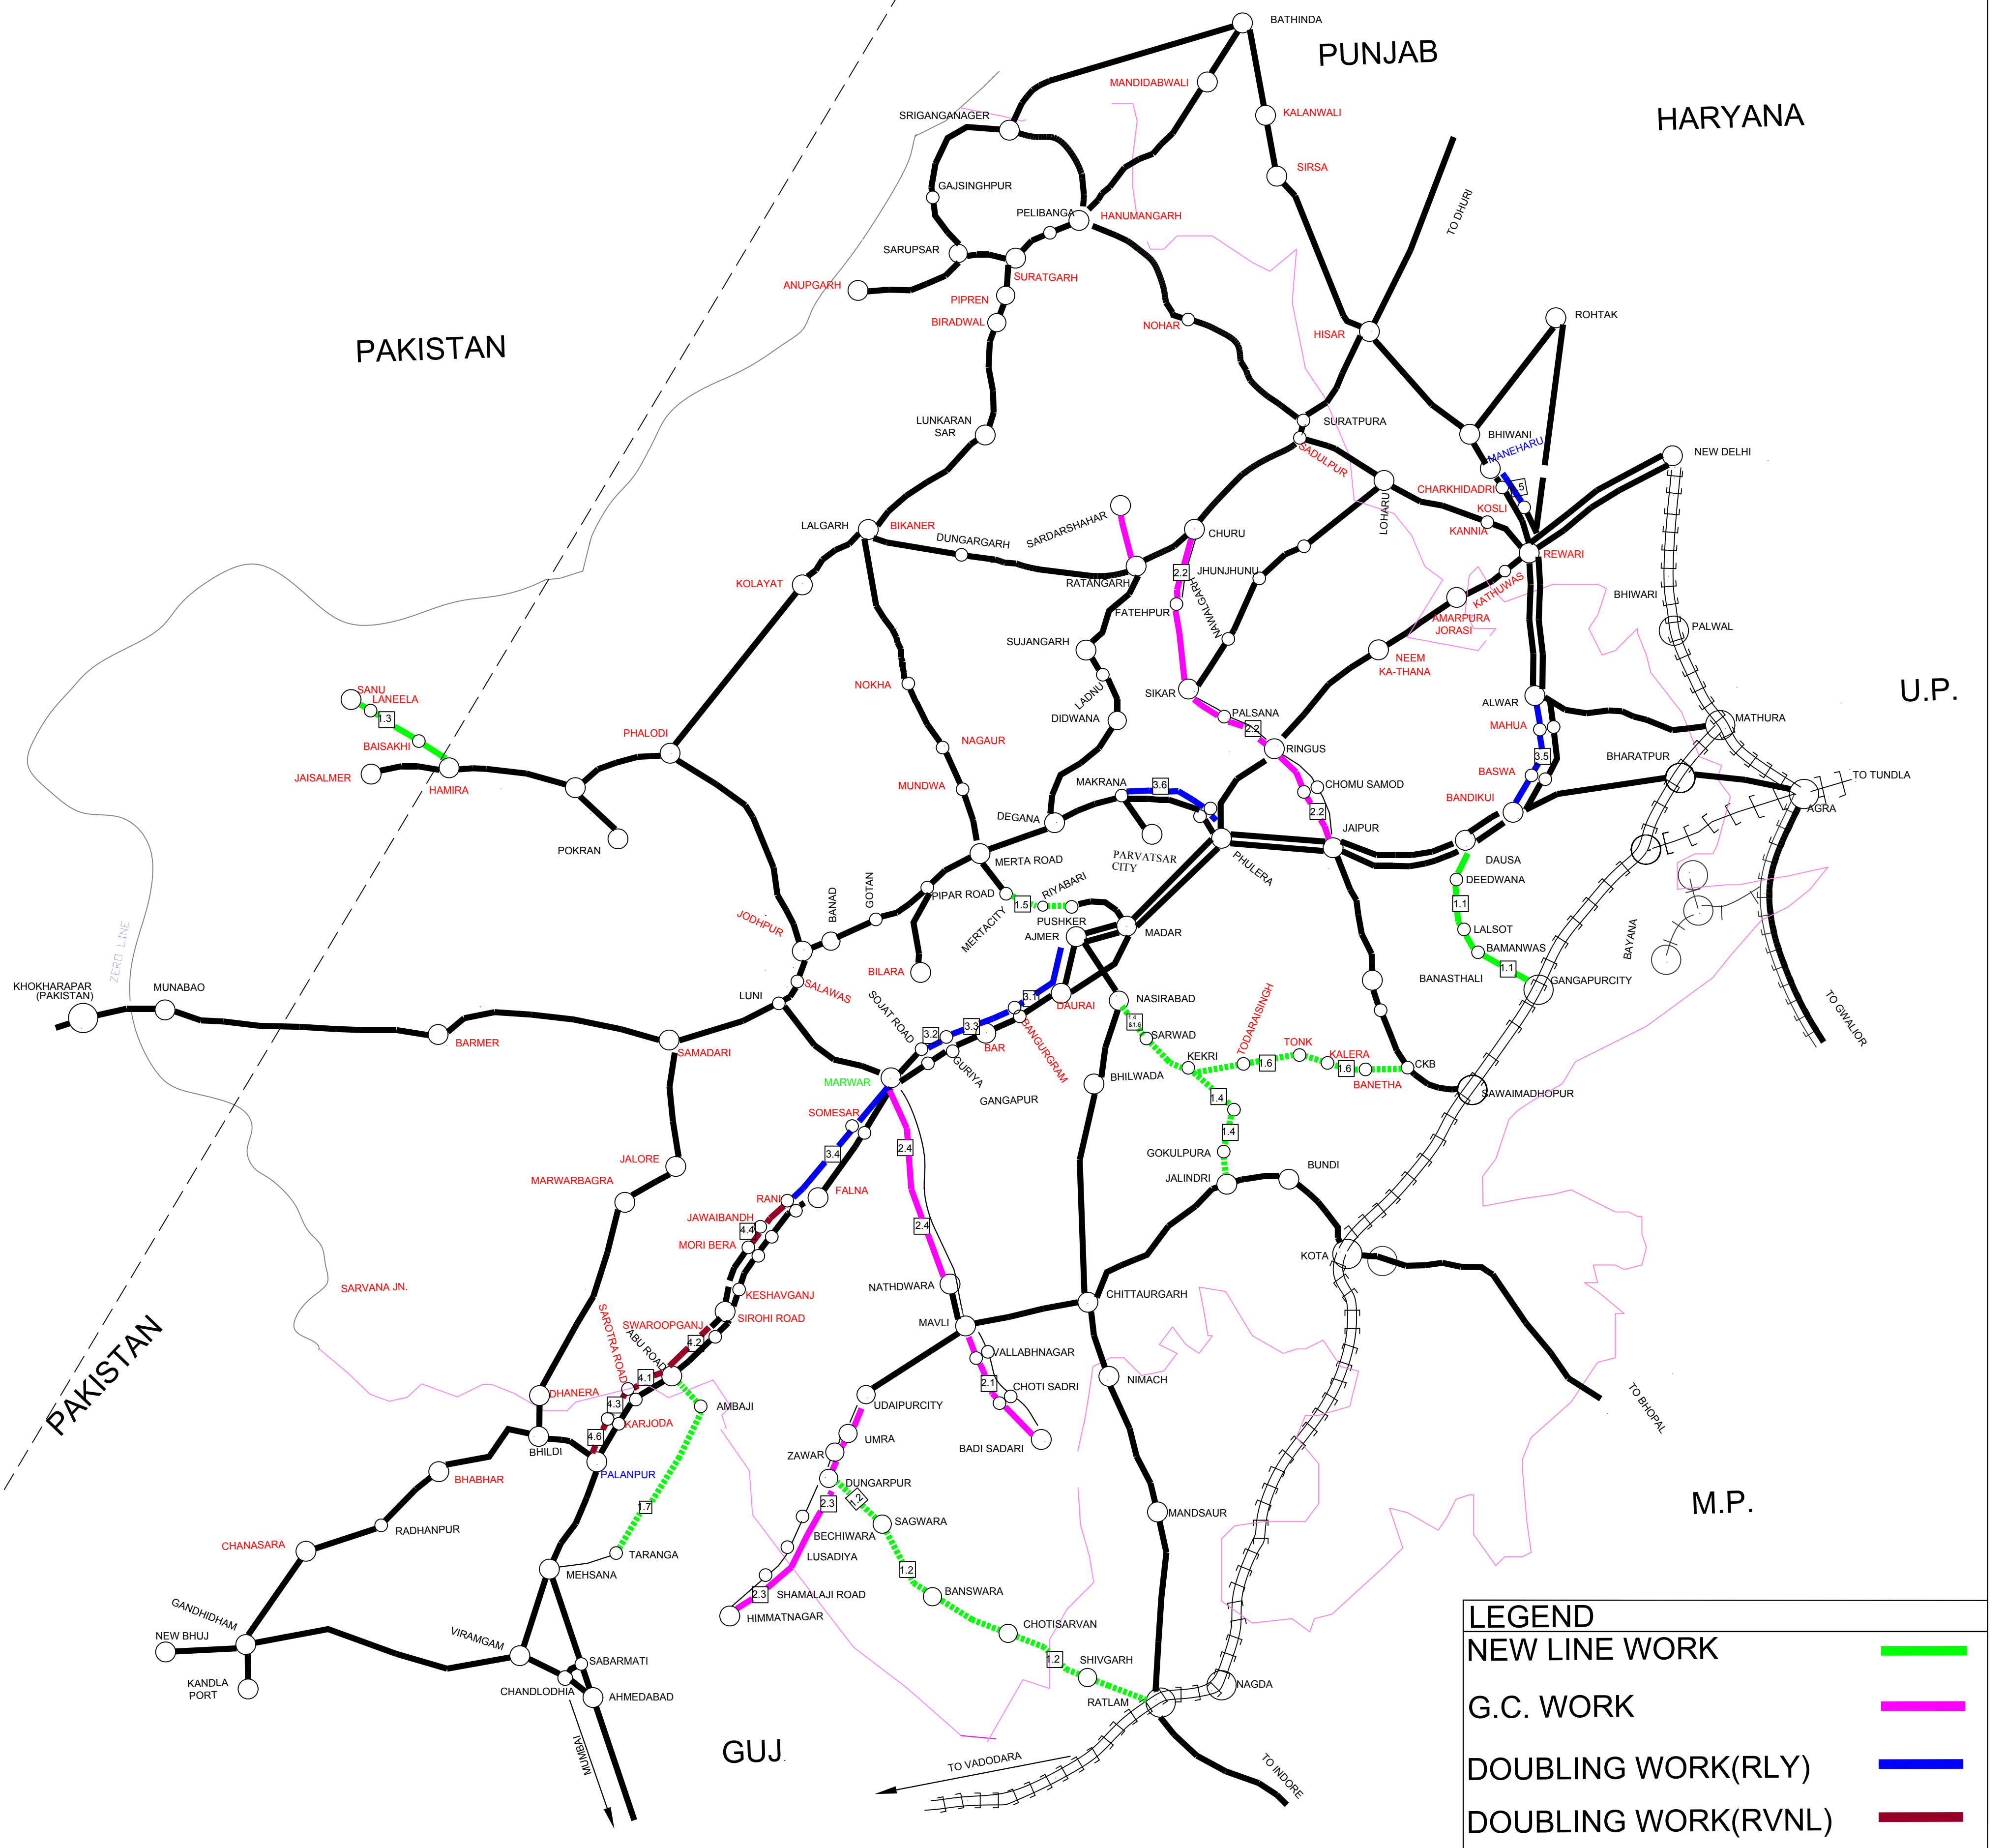

LEGEND	
NEW LINE WORK	—
G.C. WORK	—
DOUBLING WORK(RLY)	—
DOUBLING WORK(RVNL)	—
