




LIST OF SANCTIONED WORKS

Sr. No.	NAME OF WORK	SALIENT FEATURES			PHYSICAL PROGRESS & TDC
		YEAR OF SANCTION	COST IN Cr.	LENGTH IN KM	
A. NEW LINE					
1	DAUSA - GANGAPUR CITY NEW LINE Dausa-Deedwana, CRS done on 17 & 18.08.2017. GGC - Piplai, CRS done on 09.03.2021. Piplai - Laisot, CRS done on 03.03.2023.	1996-97	950.00	94.65	Laisot-Deedwana = 95% (TDC: 29.02.2024)
2	RATLAM - DUNGARPUR via BANSWARA	2011-12	4500.00	188.85	RB has de-frozen the project vide letter dt. 22.05.23. Tender awarded.
3	AJMER(NASIRABAD) - KOTA (JALINDRI)	2013-14	822.00	145.00	Execution of work kept in abeyance by RB on 24.09.2019.
4	AJMER (All)- SAWAI MADHOPUR (SWM) via TONK Bankability study report sent to RB in July-2021 with ROR (-)7.85%.	2015-16	2215.27	165.00	Cost sharing with Govt. of Rajasthan. Execution of work kept in abeyance by RB.
5	TARANGA HILL- ABU ROAD (ABR) VIA AMBAJI	2017-18	2798.16	116.65	Land acquisition is in progress. Tender awarded for 0-61 Km. (TDC: 31.12.26)
6	DEDICATED TEST TRACK FOR RDSO (i) GUDHA - THATHANA MITHRI NL (PHASE-I) (ii) RDSO DEDICATED TEST TRACK (PHASE-II)	2018-19 2019-20	353.48 466.42	22.80 37.50	75% (TDC: 31.03.24) Work is in progress. (TDC: 30.09.25)
7	NATHDWARA - NATHDWARA TOWN NEW LINE	2018-19	166.33	9.60	Land acquisition is in progress. (TDC: 30.06.26)
8	NIMACH-BADI SADRI NEW LINE	2017-18	495.18	48.35	Land acquisition is in progress. Tender awarded. (TDC: 30.06.26)
9	PUSHKAR -MERTA NEW LINE	2023-24	799.64	51.35	DPR sanctioned on 13.02.2024.
10	RAS -MERTA CITY NEW LINE (Incl. MTD bypass)	2023-24	947.00	55.90	DPR sanctioned on 13.02.2024.
B. GAUGE CONVERSION					
11	DEVGARH-NATHDWARA (82.54 KM) GC PART OF MARWAR - MAVLI	2017-18	968.92	82.54	DPR sanctioned by RB on 24.01.23. Land acquisition is in progress. Tender awarded. (TDC: 31.01.27)
C. DOUBLING					
12	PHULERA - DEGANA DOUBLING	2015-16	701.81	108.00	Balance (i) KMNC-NAC (16 Km) = 90% (TDC= Feb-24) (ii) NAC-GVMR (8 Km) = 75% (TDC= Mar-24)
13	BHATINDA - DEGANA DOUBLING	2020-21	4800.00	480.00	Work is kept in abeyance by RB vide letter dt. 26.10.2021.
14	SAWAI MADHOPUR -BYEPASS LINE	2020-21	239.54	13.54	DPR sanctioned by RB on 09.12.22. Land acquisition is in progress. Tender awarded. (TDC: 31.12.25)
15	REWARI-KATHUWAS DOUBLING	2022-23	352.41	27.73	DPR sanctioned by RB on 03.02.23. Tender awarded. (TDC: 30.06.25)
16	CHURU-RATANGARH DOUBLING	2022-23	422.60	42.81	DPR sanctioned by RB on 03.02.23. Tender awarded. (TDC: 30.06.25)
17	BHIWANI - DHOB BAHALI DOUBLING	2022-23	471.06	42.30	DPR sanctioned by RB on 27.02.23. Tender awarded. (TDC: 30.06.25)
18	MANHERU - BHIWANI KHERA DOUBLING	2022-23	413.09	31.50	DPR sanctioned by RB on 10.04.23. Tender awarded. (TDC: 30.06.25)
19	KATHUWAS - NARNAUL DOUBLING	2022-23	313.31	24.12	DPR sanctioned by RB on 10.04.23. Tender awarded. (TDC: 30.06.25)
20	CHURU - SADULPUR DOUBLING	2023-24	468.64	57.82	DPR sanctioned by RB on 29.01.24.
21	JAIPUR - SAWAI MADHOPUR DOUBLING	2023-24	1203.89	131.27	DPR sanctioned by RB in Feb-2024.
22	AJMER - CHANDERIYA DOUBLING	2023-24	1634.79	178.28	DPR sanctioned by RB in Feb-2024.
23	LUNI - SAMDARI - BHILDI DOUBLING	2023-24	3085.59	271.97	DPR sanctioned by RB in Feb-2024.
D. CAPITAL INVESTMENT (JV awaited with GOR)					
24	KISHANGARH - PARBATSAR NEW LINE	2016-17	900.00	45.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.
25	JAISALMER - BHABAR NEW LINE	2016-17	5000.00	339.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.

SYSTEM MAP
SANCTIONED NL/GC/DL WORKS (IN PROGRESS)

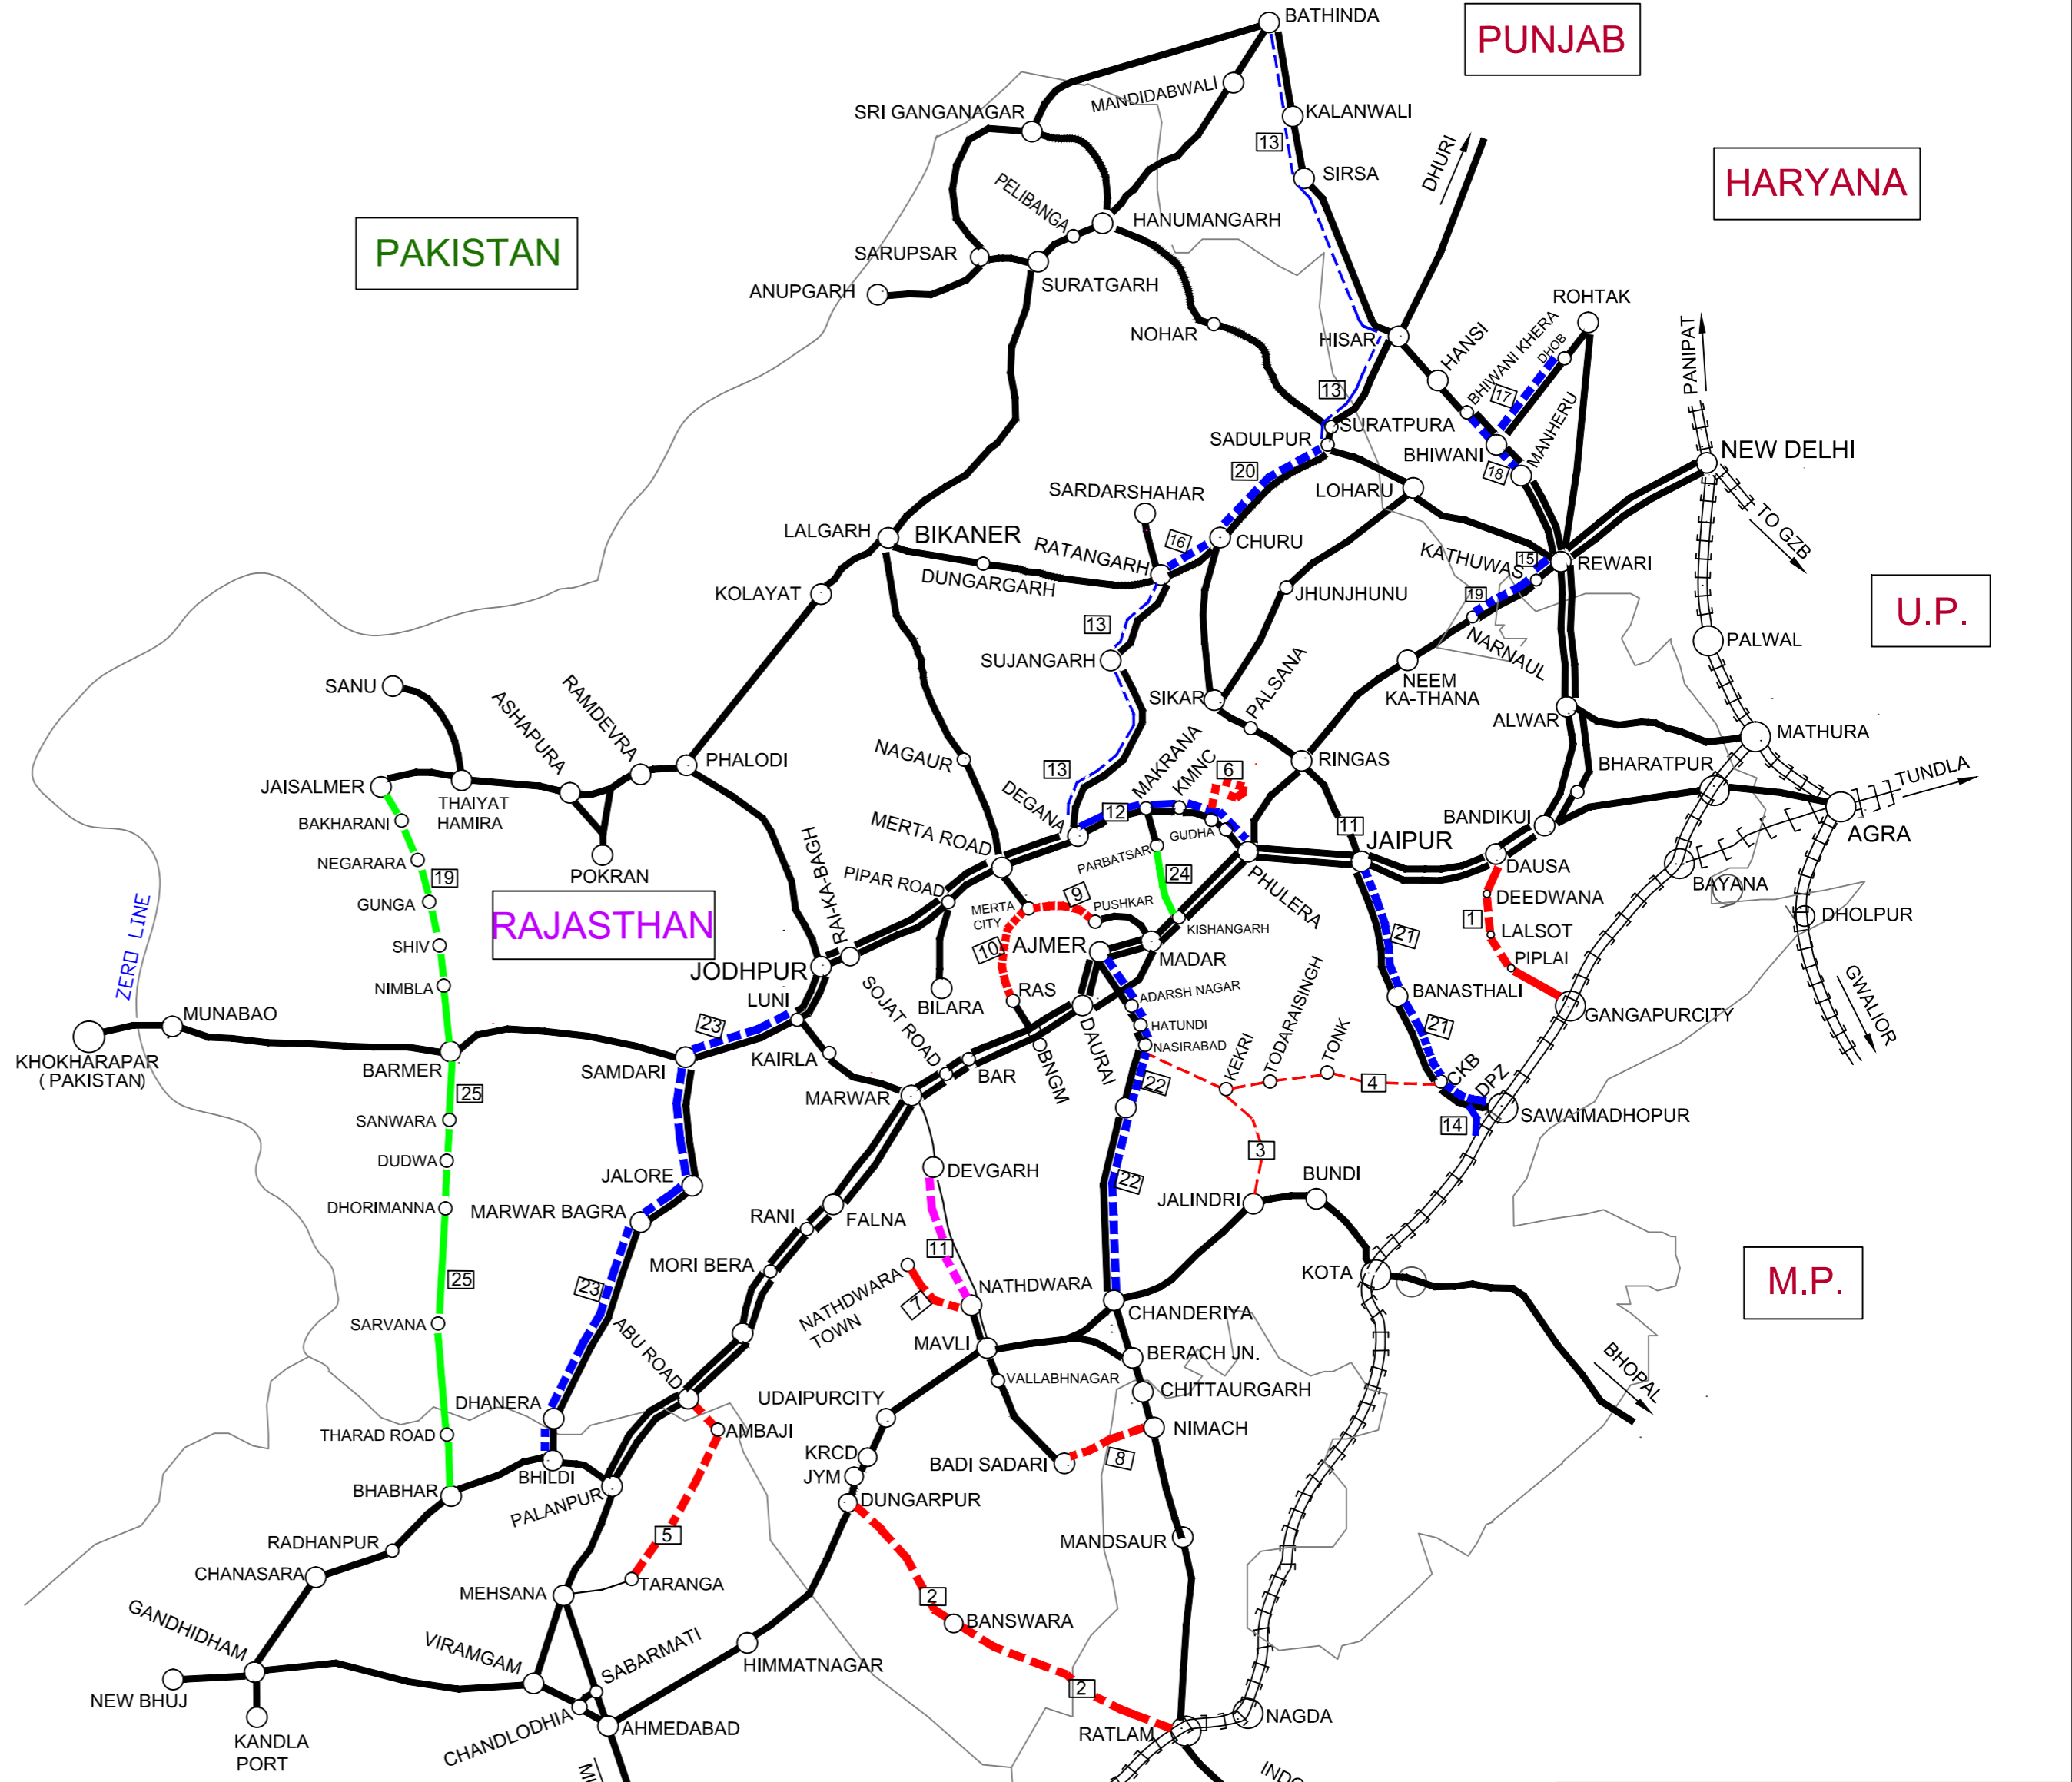

LEGEND

1. NEW LINE (Sanctioned & in progress)	---
2. NEW LINE (Sanctioned & Completed)	---
3. GC Works (Sanctioned & in progress)	---
4. GC Works (Sanctioned & Completed)	---
5. DOUBLING (Sanctioned & in progress)	---
6. DOUBLING (Sanctioned & Completed)	---
7. Kept in abeyance works :-	
NL Works	---
GC Works	---
DL Works	---
8. CAPITAL INVESTMENT (Sanctioned)	---
