
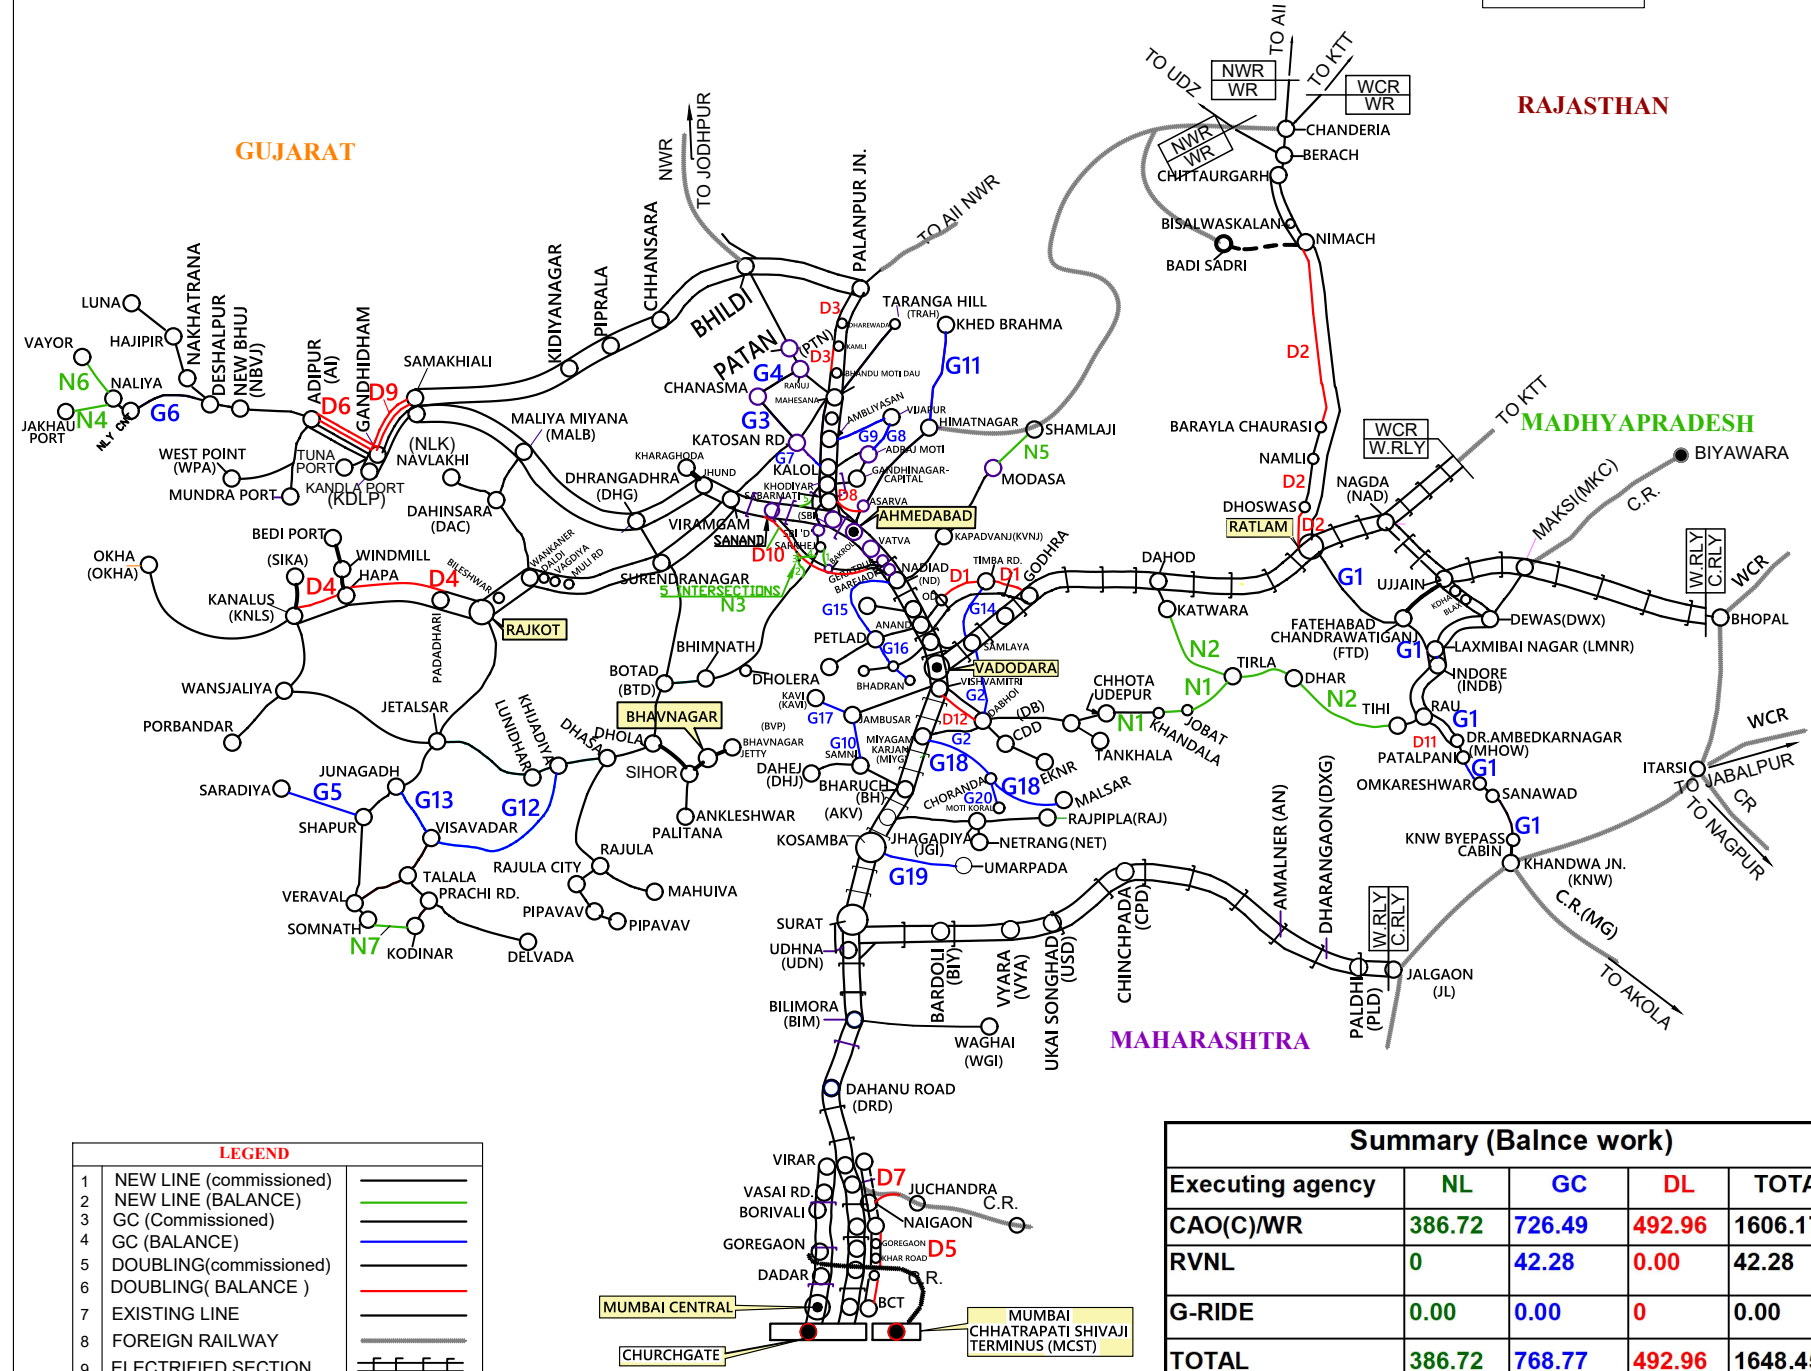


# WESTERN RAILWAY(CONSTRUCTION) MAP SHOWING THE ONGOING PROJECTS UNDER WR ( AS ON 09.08.2024 )



SR. No	NAME OF THE PROJECT	LENGTH IN KM	COMPLETED LENGTH IN KM	BALANCE LENGTH IN KM	AGENCY/CE in charge	TDC
<b>NEW LINES</b>						
N1	CHHOTA UDEPUR-DHAR	157.00	72.34	84.66	CPM-BRC	Dec-26
N2	DAHOD-INDORE	204.76	32.30	172.46	CE-C-III-CCG & CE-C-IV-CCG	Feb-27
N3	INTERSECTIONS(5) BET. GERATPUR-SANAND AND BOTAD-ADI	16.51	0.00	16.51	CPM-I-ADI	Feb-27
N4	NALIYA-JAKHAU PORT	24.88	0.00	24.88	CPM-II-ADI	Sep-26
N5	MODASA-SHAMLAJI NL (MM of ADI-HMT-UDZ)	26.65	0.00	26.65	CPM-I-ADI	Mar-25
N6	NALIYA-VYOR NL	24.65	0.00	24.65	CPM-C-II-ADI	Sep-26
N7	SOMNATH-KODINAR- NL (MM of RJT-VRL)	36.91	0.00	36.91	CPM-C-II-ADI	Not Fixed
<b>TOTAL (NL)</b>		<b>491.36</b>	<b>104.64</b>	<b>386.72</b>		
<b>DOUBLING</b>						
D1	ANAND-GODHRA	78.80	16.95	61.85	CPM-C-BRC	Dec-24
D2	NIMACH-RATLAM	133.00	23.55	109.45	CE-C-III-CCG	Jan-25
D3	MAHESANA-PALANPUR	65.10	44.93	20.17	CPM-I-ADI	Aug-24
D4	RAJKOT-KANALUS (PM-FS-99)	111.20	24.80	86.40	CPM-II-ADI	Jun-25
D5	6TH LINE BETWEEN BCT-BVI	29.53	8.71	20.82	CE-C-I-CCG	Dec-27
D6	GANDHIDHAM- ADIPUR QUADRUPLING	10.69	0.00	10.69	CPM-II-ADI	Oct-25
D7	VASAI BYPASS DOUBLE LINE BETWEEN NAIGAON AND JUCHANDRA	5.73	0.00	5.73	CE-C-I-CCG	Mar-26
D8	PROVISION OF Y CONNECTIVITY BET. SABARMATI A CABIN AND ASARVA	0.90	0.00	0.9	CPM-I-ADI	Jun-25
D9	SAMAKHIALI – GANDHIDHAM QUADRUPLING	106.00	0.00	106.00	CPM-II-ADI	Dec-26
D10	GERATPUR-SANAND 4 TH LINE	38.20	0.00	38.20	CPM-I-ADI	Feb-27
D11	RAU-DR.AMBEKKARNAGAR DL	11.39	11.39	0.00	CE-C-IV-CCG	Commi. On May 2024
D12	VISHVAMITRI-DABHOI	32.75	0.00	32.75	CPM-C-BRC	Not Fixed
<b>TOTAL (DL)</b>		<b>623.29</b>	<b>130.33</b>	<b>492.96</b>		
<b>GAUGE CONVERSION</b>						
G1	RATLAM-MHOW-KHANDWA	303.95	218.43	85.52	CE-C-IV-CCG	Feb-27
G2	MIYAGAM-SAMLAYA	96.46	32.30	64.16	CPM-C-BRC	Oct-25
G3	KATOSAN ROAD- CHANASMA	51.72	51.72	0.00	G RIDE	Completed commi. yet to be done
G4	CHANASMA-RANUJ	12.84	12.84	0.00	G RIDE	Completed commi. yet to be done
G5	SHAPUR-SARADIYA GC (MM of RJT-VRL)	46.00	0.00	46.00	CPM-C-II-ADI	Not Fixed
G6	BHUJ-NALIYA	101.35	101.35	0.00	CPM-C-II-ADI	Completed commi. yet to be done
G7	KALOL-KADI-KATOSAN ROAD	37.23	26.23	11.00	CPM-C-II-ADI	Aug-24
G8	ADRAJ MOTI- VIJAPUR	39.75	0.00	39.75	CPM-I-ADI	Jun-25
G9	VIJAPUR- AMBALIYASAN	41.53	0.00	41.53	CPM-I-ADI	Feb-25
G10	SAMNI- JAMBUSAR	24.08	0.00	24.08	CPM-C-BRC	Apr-26
G11	HIMMATNAGAR-KHEDBRAHMA	56.83	0.00	56.83	CPM-I-ADI	Feb-25
G12	KHIJADIYA- VISAVADAR	91.27	0.00	91.27	CPM-I-ADI	Oct-25
G13	JUNAGADH- VISAVADAR-RVNL	42.28	0.00	42.28	RVNL	Jan-26
G14	SAMLAYA-TIMBA ROAD	53.53	0.00	53.53	CPM-C-BRC	Jul-26
G15	NADIAD-PETLAD	37.26	0.00	37.26	CPM-C-BRC	Dec-25
G16	PETLAD-BHADRAN	22.50	0.00	22.50	CPM-C-BRC	Dec-25
G17	JAMBUSAR-KAVI	26.36	0.00	26.36	CPM-C-BRC	Apr-26
G18	MIYAGAM KARAJAN- CHORANDA-MALSAR	38.00	0.00	38.00	CPM-C-BRC	Jul-26
G19	KOSAMBA-UMARPADA	69.70	0.00	69.70	CE-C-I-CCG	Jul-27
G20	CHORANDA-MOTI KORAL	19.00	0.00	19.00	CPM-C-BRC	Dec-26
<b>TOTAL (GC)</b>		<b>1211.64</b>	<b>442.87</b>	<b>768.77</b>		

Executing agency	NL	GC	DL	TOTAL
CAO(C)/WR	386.72	726.49	492.96	1606.17
RVNL	0	42.28	0.00	42.28
G-RIDE	0.00	0.00	0	0.00
<b>TOTAL</b>	<b>386.72</b>	<b>768.77</b>	<b>492.96</b>	<b>1648.45</b>
