

SUMMARY OF SANCTIONED WORKS OVER NWR

AS ON 01.04.2022

S.N.	P.H.	SCOPE (KM)	TARGET 22-23 (KM)	BALANCE AS ON 01.04.2023 (KM)	KEPT IN ABEYANCE
1.	NL	874.73	34.51	838.23	557.85
2.	GC	189.00	37.00	152.00	-
3.	DL	1058.25	127.00	931.25	752.00
TOTAL		1658.96	198.51	1460.45	981.82

LIST OF SANCTIONED WORKS OVER NWR


Sr. No.	NAME OF WORK	SALIENT FEATURES			PHYSICAL PROGRESS & TDC
		YEAR OF SANCTION	COST IN Cr.	LENGTH IN KM	
1.0 NEW LINE					
1.1	DAUSA (DO) - GANGAPUR CITY (GGC) DO-Deedwana CRS done on 17.08.17 & 18.08.17. GGC - PIPLAI CRS done on 09.03.21.	1996-97	950.00	94.65	90% Piplai-Lalsot (TDC: 31.12.22) Lalsot-Deedwana (31.03.23)
1.2	RATLAM(RTM)-DUNGARPUR(DNRP) Via-BANSWARA(BNSW) Bankability study report sent to RB in Feb'20.	2011-12	4500.00	188.85	6.25% Execution of work kept in abeyance by RB.
1.3	AJMER(NASIRABAD) - KOTA (JALINDRI) CCEA sanction is yet to be obtained by Rly Bd.	2013-14	822.00	145.00	Execution of work kept in abeyance by RB.
1.4	PUSHKAR (POHT) - MERTA (MTD) CCEA sanction is yet to be obtained by Rly Bd.	2013-14	323.00	59.00	Execution of work kept in abeyance by RB.
1.5	AJMER (AII)- SAWAI MADHOPUR (SWM) VIA TONK	2015-16	2215.27	165.00	Execution of work kept in abeyance by RB.
1.6	TARANGA HILL- ABU ROAD (ABR) VIA AMBAJI	2017-18	2798.16	116.65	DPR sanctioned on 21.07.2022.
1.7	DEDICATED TEST TRACK FOR RDSO				
	(i) GUDHA - THATHANA MITHRI NL (PHASE-I)	2018-19	353.48	25.00	42% (TDC: 31.12.2023)
	(ii) RDSO DEDICATED TEST TRACK (PHASE-II)	2019-20	466.42	34.00	DPR sanctioned on 18.11.2021
1.8	NATHDWARA - NATHDWARA TOWN NEW LINE	2018-19	166.33	9.60	LA is in progress.
1.9	NIMACH-BADI SADRI NEW LINE	2017-18	495.18	48.35	LA is in progress.
2.0	GANGAPUR - SIMUTTRA NEW LINE	2010-11	1250.00	75.64	Work allotted to NWR on 17.05.2022 by RB.
2.0 GAUGE CONVERSION WORKS					
2.1	JAIPUR-SIKAR & SIKAR-CHURU SECTION COMMISSIONED (i) Section already commissioned. (ii) Status of 05 new X-ing Stations :- Rashidpur Khori, Kayamsar, Baori Thikaria & Goriya new crossing stations stations commissioned. Work in progress at Chhota Gudha new crossing station (Nov-22)	2008-09	658.07	320.04	100% (PROJECT ALREADY COMMISSIONED) Work in progress at Chhota Gudha new crossing station (Nov-22)
2.2	HIMMATNAGAR (HMT) - UDAIPUR (UDZ) (i).RGQ-HMT, CRS authorization issued on 31.05.19. (ii).UDZ-KRCD, CRS authorization issued on 17.01.20. (iii).RGQ - DNRP, CRS authorization issued on 23.12.20. (iv) DNRP-JYM, CRS authorization issued on 23.03.22. (v) JYM-KRCD, CRS done on 08 & 09.07.2022.	2008-09	1648.18	208.48	100%
2.3	MARWAR (MJ) - MAVLI (MVJ) (NATHDWARA)	2017-18	968.92	82.54	DPR sent to RB on 04.08.2022.
3.0 DOUBLING					
3.1	PHULERA (FL) - DEGANA (DNA) (i) DNA-BOW : COMMISSIONED ON 27.10.2021. (ii) BOW-KMNC : COMMISSIONED ON 15.03.2022.	2015-16	701.81	108.00	75% KMNC-NAC 31.01.2023 NAC-FL 28.02.2023
3.2	DEGANA (DNA)-RAIKA BAGH (RKB) (i) DNA-MTD : COMMISSIONED ON 24.12.2021. (ii) MTD-KXG : COMMISSIONED ON 25.02.2022. (iii) KXG-PPR : COMMISSIONED ON 21.06.2022.	2018-19	808.85	145.00	90% PPR-RKB 31.12.2022
3.3	JAIPUR - SAWAI MADHOPUR DOUBLING	2019-20	1046.30	131.27	Revised DPR sent to RB on 15.11.2021.
3.4	BHATINDA - BHILDI VIA HISAR, RATANGARH DEGANA, LUNI, SAMDARI (EXCL. DEGANA -RAI KA BAGH)	2020-21	7522.00	752.00	Work is kept in abeyance For LN-BLDI (271.97 Km) & BTI-DNA (480.0 Km). Revised DPR of patch doubling of Dudia-Samdari, Samdari-Mokalsar, Mokalsar- Jalore, Jalore- Modran, Modran- Marwar Bhinmal sent to RB on 05.08.22.
3.5	AJMER-CHITTORGARH DOUBLING	2020-21	1860.00	186.00	DPR sent to RB on 14.06.2021
3.6	SAWAI MADHOPUR -BYEPASS LINE	2020-21	251.64	13.54	DPR sent to RB on 06.07.2022.

NORTH WESTERN RAILWAY

AS ON 05.10.2022

SYSTEM MAP

SANCTIONED WORKS (IN PROGRESS)

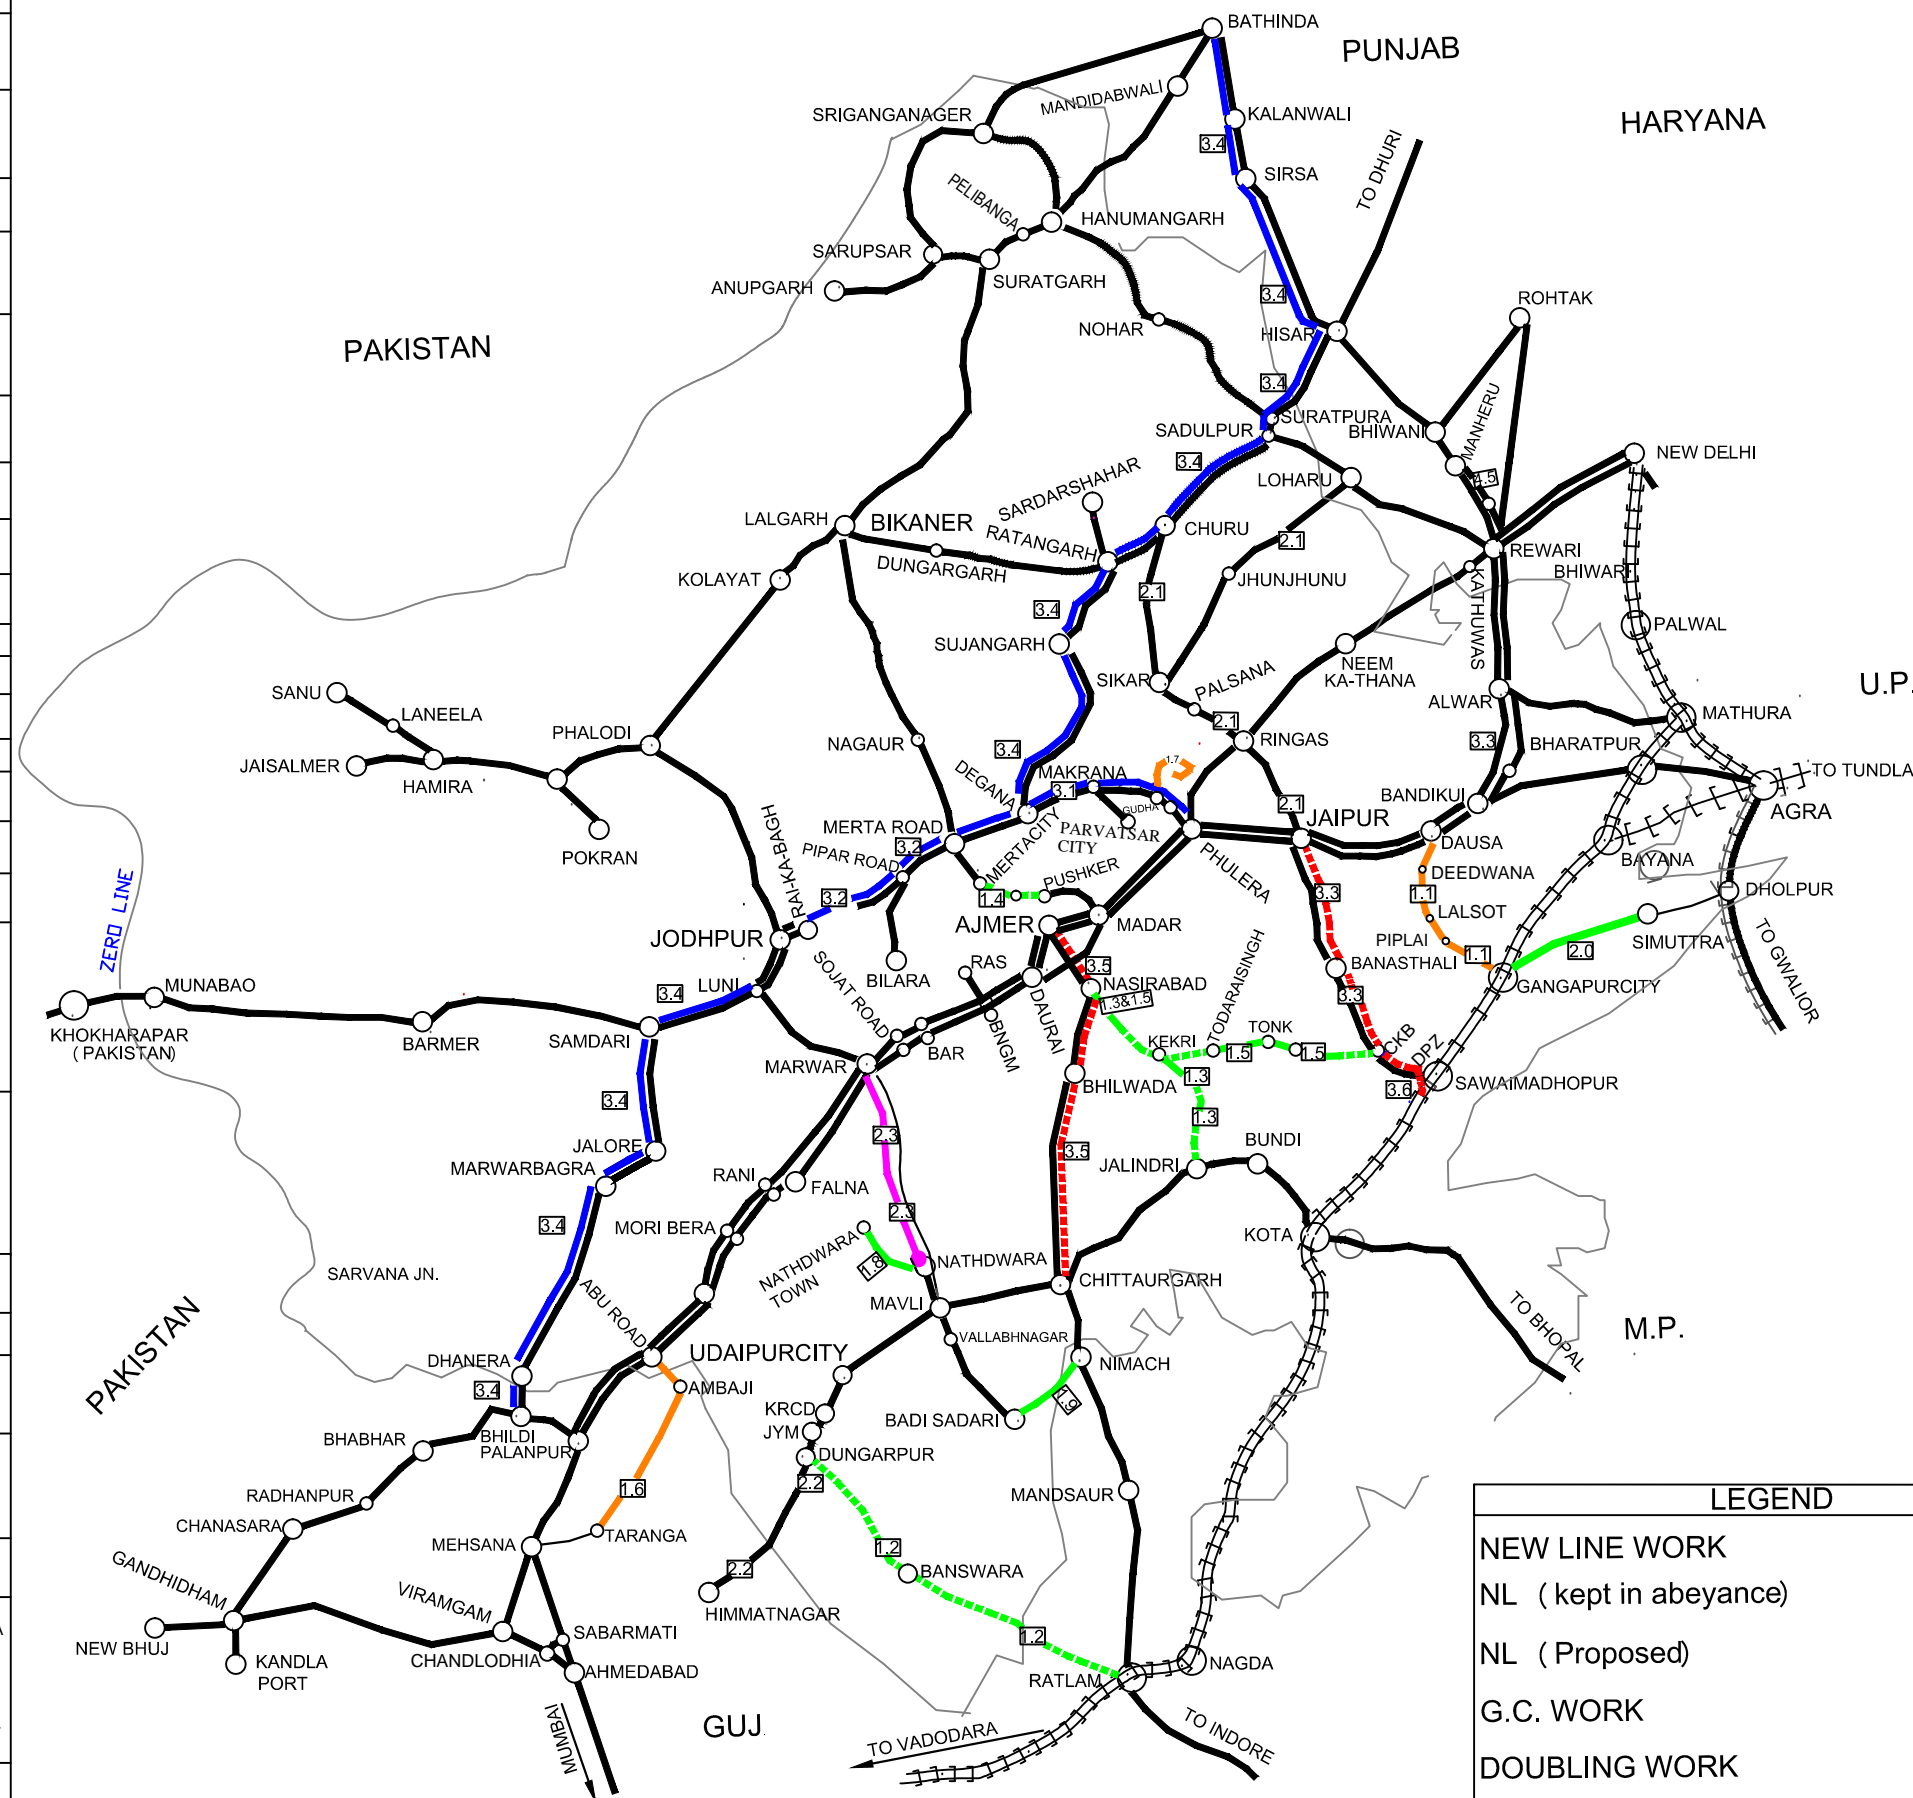

LEGEND

NEW LINE WORK	Orange solid line
NL (kept in abeyance)	Green dashed line
NL (Proposed)	Green solid line
G.C. WORK	Pink solid line
DOUBLING WORK	Blue solid line
DOUBLING (DPR not sanction)	Red dashed line
