


**LEGEND**

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

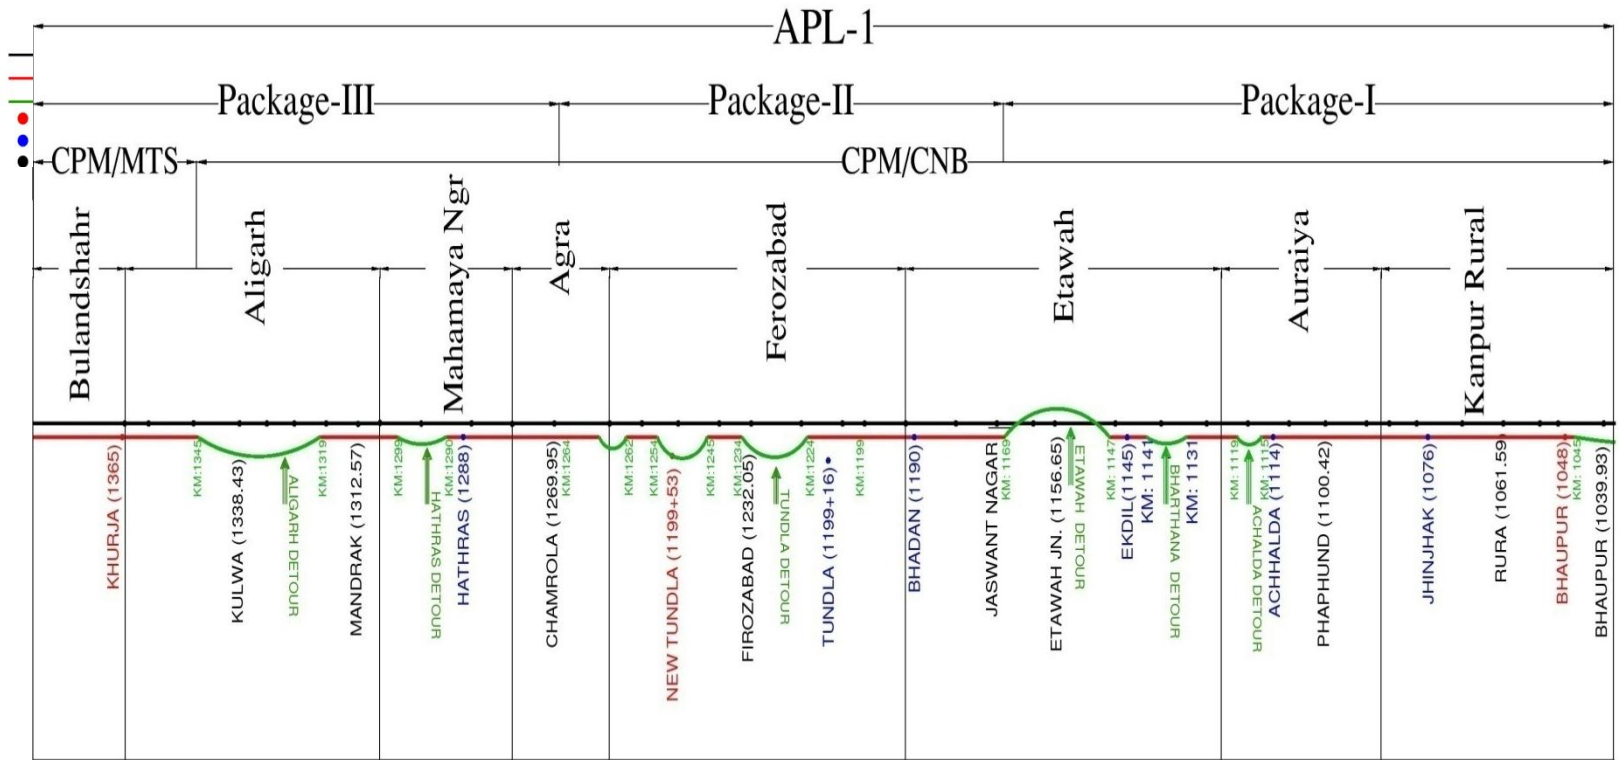

**EDFC - APL-1 (Land Acquisition Progress for the Month of November 2013)**

Scope	( Kms)	15	45	42	24	66	64	33	55
	Area (Ha.)	59	233	170	78	234	293	109	144
20A (Ha.)	59	233	170	78	234	293	109	144	
20E (Ha.)	59	233	170	78	234	293	109	144	
20F (Ha.)	59	233	170	78	229	293	109	144	
Award Declared (Cr.)	26	160	94	49	121	60	13	14	
Disbursed (Cr.)	11	151	90	46	119	50	12	14	
